


Major IT Report Archive for the Third Quarter of 2020

ND Information Technology
Portfolio Overview
SPONSORING AGENCY: All
PROGRAM: All
PORTFOLIO: All
PROJECT STATE: All
GOVERNANCE STAGE: All

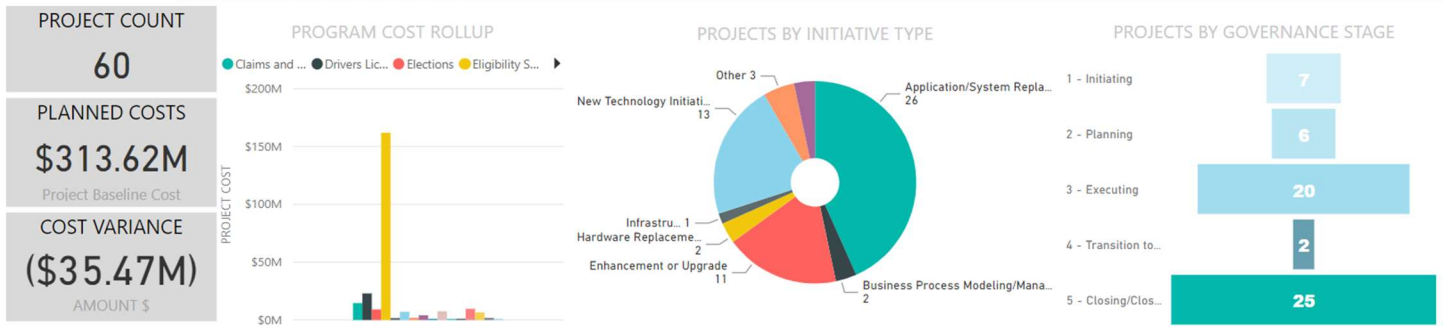

PROJECTS	% COMP	GOVERNANCE STAGE	SPONSORING AGENCY	BASELINE START	BASELINE FINISH	BASELINE or ESTIM. COST	OVERALL	TREND	SCOPE	RISK	COST	SCHEDULE
Child Care Licensing	29%	2 - Planning	Human Services	12/4/2017	6/30/2021	\$3,000,000.00	●	No Change	●	●	●	●
Electronic Benefits Transfer for Special Supplemental Nutritio...	74%	3 - Executing	Health	10/26/2017	11/5/2020	\$2,221,857.40	●	Up	●	●	●	●
Electronic Health Records	100%	3 - Executing	Human Services	5/11/2017	7/31/2020	\$6,933,982.16	●	No Change	●	●	●	●
Electronic Medical Records	60%	2 - Planning	Corrections and Rehab...	12/11/2018	6/30/2021	\$1,037,051.00	●	No Change	●	●	●	●
Electronic Visit Verification System	42%	3 - Executing	Human Services	4/16/2018	8/9/2021	\$1,416,743.07	●	No Change	●	●	●	●
Environmental Regulatory Software System	13%	3 - Executing	Environmental Quality	10/1/2019	1/26/2021	\$704,499.60	●	No Change	●	●	●	●
North Dakota Foods 4	100%	5 - Closing/Closed	Public Instruction	8/31/2018	9/30/2019	\$465,579.00	●	No Change	●	●	●	●
Statewide Parcel Dataset	69%	3 - Executing	Information Technology	7/1/2019	8/11/2021	\$589,985.01	●	No Change	●	●	●	●
Teachers Fund for Retirement Pension System Replacement	0%	1 - Initiating	Retirement and Invest...	9/2/2019	6/30/2021	\$9,139,000.00	●	Up	●	●	●	●
Claims and Policy System												
Claims and Policy System - Project 1	100%	5 - Closing/Closed	Workforce Safety and I...	7/1/2015	5/19/2016	\$1,630,288.00	●	No Change	●	●	●	●
Claims and Policy System - Release 2	100%	5 - Closing/Closed	Workforce Safety and I...	4/11/2016	9/30/2016	\$1,640,320.00	●	No Change	●	●	●	●
Claims and Policy System - Release 3	100%	5 - Closing/Closed	Workforce Safety and I...	9/19/2016	2/18/2017	\$1,355,629.00	●	No Change	●	●	●	●
Claims and Policy System - Release 4	100%	5 - Closing/Closed	Workforce Safety and I...	2/27/2017	10/31/2017	\$1,873,410.00	●	No Change	●	●	●	●
Claims and Policy System - Release 5	100%	5 - Closing/Closed	Workforce Safety and I...	10/2/2017	6/29/2018	\$1,835,649.00	●	No Change	●	●	●	●
Claims and Policy System - Release 6	100%	5 - Closing/Closed	Workforce Safety and I...	6/11/2018	5/6/2019	\$2,698,860.00	●	No Change	●	●	●	●
Claims and Policy System - Release 7	100%	5 - Closing/Closed	Workforce Safety and I...	5/13/2019	8/28/2020	\$2,502,194.20	●	Up	●	●	●	●
Claims and Policy System - Release 8	12%	3 - Executing	Workforce Safety and I...	5/26/2020	6/18/2021	\$2,658,946.40	●	No Change	●	●	●	●
Drivers License System Replacement												
Drivers License Business Process Modeling	100%	5 - Closing/Closed	Transportation	10/16/2019	3/30/2020	\$240,000.00	●	No Change	●	●	●	●
Drivers License Mobile Application	66%	1 - Initiating	Transportation	6/19/2020	12/31/2020	\$487,300.00	●	No Change	●	●	●	●
Drivers License System Implementation	3%	1 - Initiating	Transportation	2/3/2020	5/9/2022	\$22,283,650.50	●	No Change	●	●	●	●
Elections												
Electronic PollBook System	57%	3 - Executing	Secretary of State	11/12/2019	12/18/2020	\$2,039,575.00	◆	No Change	◆	◆	●	●
Voting System Replacement	100%	4 - Transition to ...	Secretary of State	6/28/2019	5/28/2020	\$7,192,282.00	●	No Change	●	●	●	●
Eligibility Systems Modernization												
Eligibility Systems Modernization - Release 1	100%	5 - Closing/Closed	Human Services	5/7/2012	5/18/2016	\$50,943,770.00	●	No Change	●	●	●	●
Eligibility Systems Modernization - Release 2	100%	5 - Closing/Closed	Human Services	2/1/2016	6/28/2019	\$108,469,338.00	●	No Change	●	●	●	●
Eligibility Systems Modernization - Release 3	100%	5 - Closing/Closed	Human Services	5/1/2019	9/16/2020	\$9,401,330.32	●	No Change	●	●	●	●
Eligibility Systems Modernization - Release 4	12%	3 - Executing	Human Services	6/1/2020	12/29/2021	\$5,076,428.76	●	No Change	●	●	●	●
Enterprise Service Management (ESM)												
Enterprise Service Management Asset and Configuration Man...	24%	2 - Planning	Information Technology				●	No Change	●	●	?	●
Enterprise Service Management Service Catalog Implementati...	23%	2 - Planning	Information Technology	6/18/2020	12/22/2020	\$600,000.00	●	No Change	●	●	●	●
ESM Phase 1 Minimum Viable Product (MVP)	100%	3 - Executing	Information Technology	2/4/2020	7/29/2020	\$493,010.00	●	No Change	●	●	●	●
Medicaid Management Information System (Health Enterp...												
Medicaid Management Information System (Health Enterpris...	0%	1 - Initiating	Human Services	7/2/2018	6/30/2021	\$7,104,000.00	●	No Change	●	●	●	●
myWSI												
myWSI - Release 3	100%	5 - Closing/Closed	Workforce Safety and I...	7/15/2019	9/1/2020	\$599,312.00	●	Up	●	●	●	●
myWSI - Release 4	21%	3 - Executing	Workforce Safety and I...	6/17/2020	6/18/2021	\$303,350.00	●	No Change	●	●	●	●
myWSI - Releases 1-2	100%	5 - Closing/Closed	Workforce Safety and I...	7/3/2017	6/14/2019	\$1,032,409.00	●	No Change	●	●	●	◆
ND Health Information Network												
NDHIN Customer Relationship Management Tool	100%	5 - Closing/Closed	Information Technology	2/14/2020	6/29/2020	\$87,605.40	●	No Change	●	●	●	◆
NDHIN Expansion Project - Cancer Registry	43%	3 - Executing	Information Technology	8/31/2020	3/19/2021	\$186,000.00	●	No Change	●	◆	●	●
NDHIN Expansion Project - eMPI and eHPD	37%	3 - Executing	Information Technology	10/14/2019	1/22/2021	\$186,000.00	●	Up	●	●	●	●
NDHIN Expansion Project - Encounters Alerts and Notifications	53%	3 - Executing	Information Technology	10/14/2019	2/17/2021	\$139,500.00	●	Up	●	◆	●	●
NDHIN Expansion Project - Public Health Assessment	37%	3 - Executing	Information Technology	11/27/2019	2/25/2021	\$204,600.00	●	Up	●	◆	●	●
NDHIN Expansion Project - SMHP	100%	3 - Executing	Information Technology	10/14/2019	7/9/2020	\$108,500.00	●	Up	●	●	●	●
NDHIN Expansion Project - Sustainability	65%	3 - Executing	Information Technology	10/14/2019	8/12/2021	\$108,500.00	●	Up	●	◆	●	●
North Dakota Health Information Network Orion Phase II	100%	5 - Closing/Closed	Information Technology	4/4/2019	6/12/2020	\$3,030,932.52	●	No Change	◆	●	●	●

ND Health Information Network													
NDHIN Customer Relationship Management Tool	100%	5 - Closing/Closed	Information Technology	2/14/2020	6/29/2020	\$87,605.40	●	No Change	●	●	●	●	◆
NDHIN Expansion Project - Cancer Registry	43%	3 - Executing	Information Technology	8/31/2020	3/19/2021	\$186,000.00	●	No Change	●	◆	●	●	●
NDHIN Expansion Project - eMPI and eHPD	37%	3 - Executing	Information Technology	10/14/2019	1/22/2021	\$186,000.00	●	Up	●	●	●	●	●
NDHIN Expansion Project - Encounters Alerts and Notifications	53%	3 - Executing	Information Technology	10/14/2019	2/17/2021	\$139,500.00	●	Up	●	◆	●	●	●
NDHIN Expansion Project - Public Health Assessment	37%	3 - Executing	Information Technology	11/27/2019	2/25/2021	\$204,600.00	●	Up	●	◆	●	●	●
NDHIN Expansion Project - SMHP	100%	3 - Executing	Information Technology	10/14/2019	7/9/2020	\$108,500.00	●	Up	●	●	●	●	●
NDHIN Expansion Project - Sustainability	65%	3 - Executing	Information Technology	10/14/2019	8/12/2021	\$108,500.00	●	Up	●	◆	●	●	●
North Dakota Health Information Network Orion Phase II	100%	5 - Closing/Closed	Information Technology	4/4/2019	6/12/2020	\$3,030,932.52	●	No Change	◆	●	●	●	●
Pre-School Development Grant													
Preschool Development Grant - Early Childhood Integrated D...	57%	2 - Planning	Human Services	7/1/2019	1/13/2021	\$1,036,200.00	●	Up	●	●	●	●	●
Risk Based Data Management System Upgrade													
Risk Based Data Management System Upgrade - NorthSTAR ...	100%	5 - Closing/Closed	Oil and Gas Division	10/8/2018	5/17/2019	\$1,054,099.00	●	No Change	●	●	●	●	●
Risk Based Data Management System Upgrade - NorthSTAR ...	100%	5 - Closing/Closed	Oil and Gas Division	2/1/2019	4/3/2020	\$2,637,301.00	●	No Change	●	●	●	●	●
Risk Based Data Management System Upgrade - NorthSTAR ...	60%	3 - Executing	Oil and Gas Division	1/2/2020	3/15/2021	\$4,156,272.83	●	No Change	●	●	●	●	●
Secretary of State File 2.0													
FirstStop Sub-Program Apostilles-Authentications	0%	1 - Initiating	Secretary of State	1/13/2020	2/25/2020	\$33,810.00	●	No Change	●	●	●	●	●
FirstStop Sub-Program Data List Requests	100%	4 - Transition to ...	Secretary of State	10/3/2019	11/18/2019	\$19,527.00	●	No Change	●	●	●	●	●
FirstStop Sub-Program Enhancement AR	100%	5 - Closing/Closed	Secretary of State	8/26/2019	9/23/2019	\$31,051.20	●	No Change	●	●	●	●	●
FirstStop Sub-Program Notary-Apostilles-Authentications	100%	5 - Closing/Closed	Secretary of State	12/16/2019	5/18/2020	\$98,231.00	●	No Change	●	●	●	●	●
FirstStop Sub-Program Service of Process	100%	5 - Closing/Closed	Secretary of State	7/9/2020	10/15/2020	\$19,527.00	●	No Change	●	●	●	●	●
Statewide Automated Reporting System Rewrite													
Statewide Automated Reporting System Rewrite	28%	2 - Planning	Public Instruction	3/2/2020	2/9/2021	\$1,200,000.00	●	No Change	●	●	●	●	●
Statewide Interoperability Radio Network													
Statewide Interoperability Radio Network Phase 1-Group 1	100%	5 - Closing/Closed	Information Technology	1/21/2019	8/18/2020	\$5,785,067.24	●	No Change	●	●	●	●	●
Statewide Interoperability Radio Network Phase 2-Group 1	51%	3 - Executing	Information Technology	7/29/2019	4/11/2023	\$25,582,657.00	●	No Change	●	●	●	●	●
Statewide Longitudinal Data System													
Statewide Longitudinal Data System Data Utilization Project	56%	3 - Executing	Information Technology	7/19/2016	11/4/2021	\$6,675,690.04	●	Up	●	●	●	●	●
Statewide Longitudinal Data System Modernization	0%	1 - Initiating	Information Technology				●	No Change	●	●	=	?	
Trust Lands Information Technology Systems Replacement													
Financial Management And Accounting	100%	5 - Closing/Closed	Trust Lands	1/8/2020	10/30/2020	\$1,849,455.00	●	Up	●	●	●	●	●
Land Management System	0%	3 - Executing	Trust Lands				●	No Change	●	●	=	?	
Unclaimed Property Replacement	100%	5 - Closing/Closed	Trust Lands	7/25/2018	5/3/2019	\$273,700.00	●	No Change	●	●	●	●	●
Unemployment Insurance System Modernization													
Internet Unemployment System Claimant Portal	94%	5 - Closing/Closed	Job Service North Dak...	10/29/2018	1/21/2020	\$1,150,329.90	◆	Down	◆	◆	●	●	
Unemployment Insurance Code Migration	0%	1 - Initiating	Job Service North Dak...				●	No Change	●	●	=	?	
